

Equipment Inspection Checklist

Project Name:

Checklist No.

Make:

OWN

Hired


Project Code:

Date:

Model:

Contractor

Equipment Name & Number:		AIR COMPRESSOR		
Note: Please write Yes or No in the given box and if some comments write in remarks column.				
SN.	Description		Yes/No	Remarks
1.	Physical condition of compressor tank should be good and certified by TPI.	#		
2.	Piston should be in good condition.	#		
3.	Motor should be in good and working condition.	#		
4.	Inspection date and due date should be clearly marked.	#		
5.	Pressure gauge should be in working state and free from defects.	#		
6.	Safety valve should be calibrated at regular interval.	#		
7.	Any other valve should be free from defects and in working condition.	#		
8.	Rotating part should be covered with fixed guard.	#		
9.	All joints should be properly tightened.	#		
10.	Compressor should be grounded as per IS 3043:1987.	#		
11.	Power cable should be free from defects and connection taken through industrial plug.	#		
12.	Whip arrestor is in good condition.	#		
13.	Work carried out by competent person with TPC			

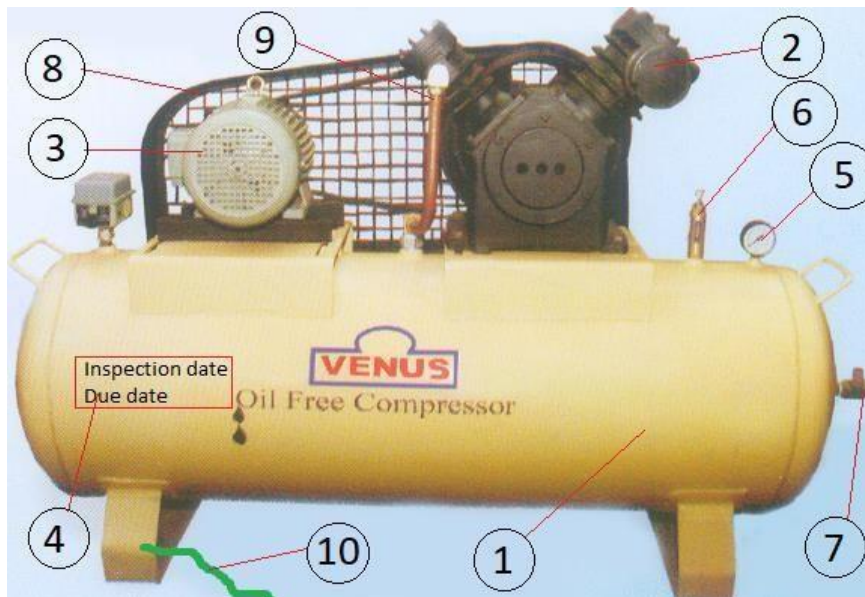

FIT	<input type="checkbox"/>	PARTIALLY FIT	<input type="checkbox"/>	UNFIT	<input type="checkbox"/>
Inspected By		Reviewed By			
Name:		Name:			
Signature with date:		Signature with date:			
