


Equipment Inspection Checklist

Project Name:
Checklist No.
Make:
OWN

Hired

Project Code:
Date:
Model:
Contractor

Equipment Name & Number:		GANTRY CRANE		
Note: Please write Yes or No in the given box and if some comments write in remarks column.				
SN.	Description		Yes/No	Remarks
1.	Machine should be physically good & Should have valid TPI certificate.	#		
2.	SWL should be visible on either side.	#		
3.	Walkaway should be in good condition and free from obstruction.			
4.	Access ladder should be provided with cage.	#		
5.	Proximity sensor should be in working condition.	#		
6.	Operator cabin should be in good condition and clean.	#		
7.	Wire sling should be free from damage.	#		
8.	Hook latch must be installed in hook.	#		
9.	Guardrail system should be provided.	#		
10.	Rotating part of motor should be covered.	#		
11.	Wire sling drum should be under canopy.	#		
12.	Audible horn should be in working condition.	#		
13.	Fire extinguisher in operator cabin.	#		
14.	Operator have suitable license & TPC.	#		
15.	Deflection test should be carried out.	#		

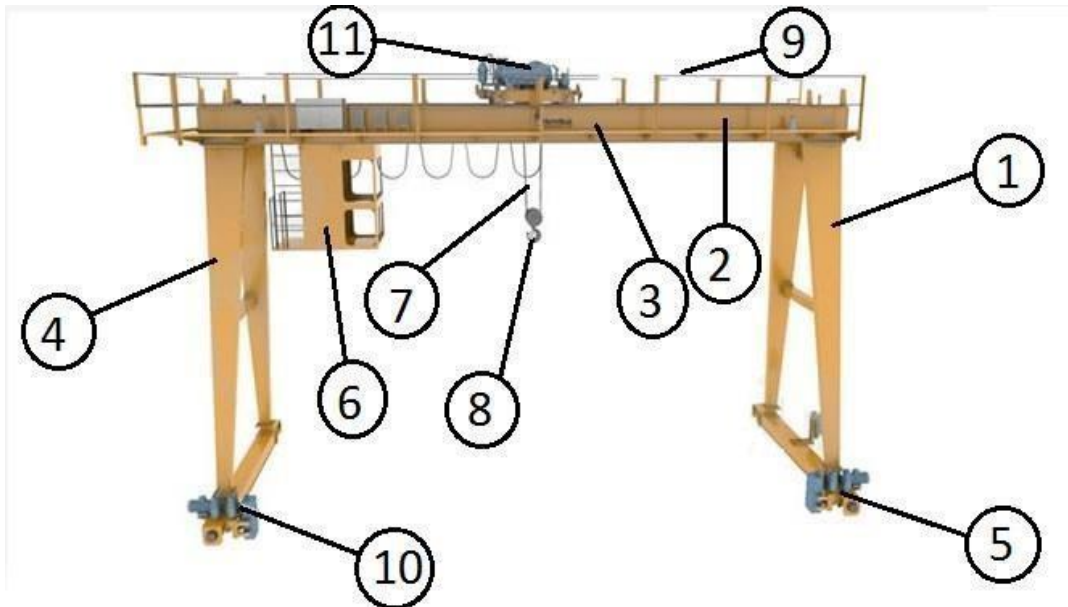

FIT	<input type="checkbox"/>	PARTIALLY FIT	<input type="checkbox"/>	UNFIT	<input type="checkbox"/>
Inspected By		Reviewed By			
Name:		Name:			
Signature with date:		Signature with date:			
